

City Walk

The project is complete.

Close-out audits with NCDOT are underway.








Riverwalk

Construction is expected to be finished this summer.


The bridge is currently at 90%






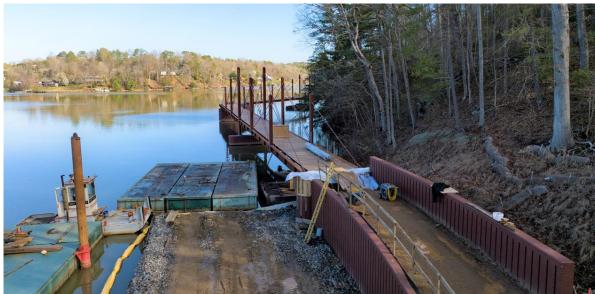



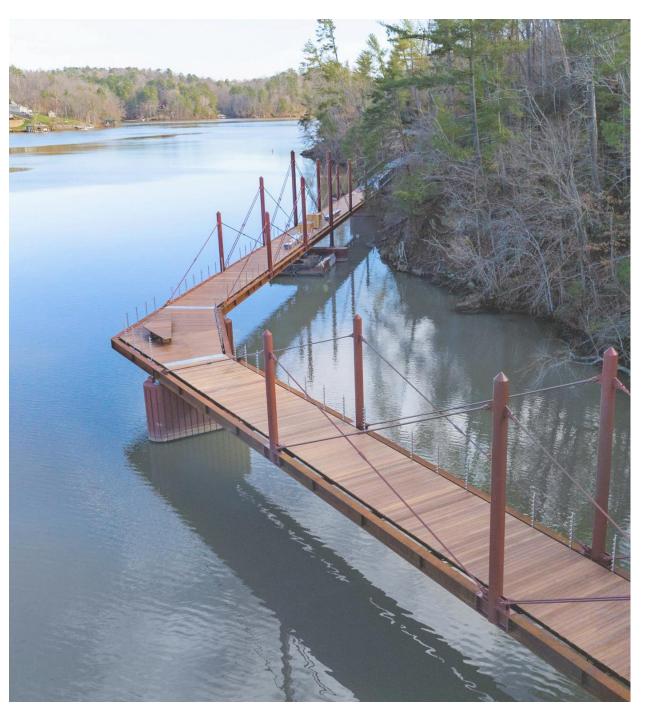



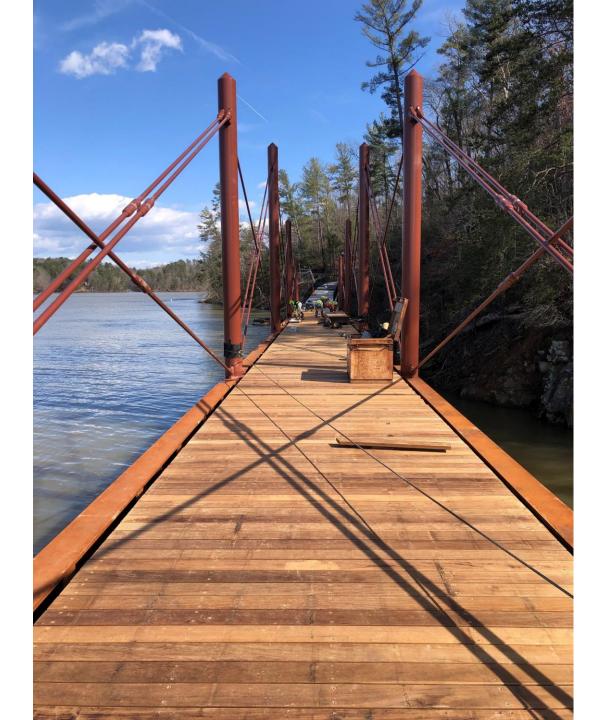



Aviation Walk

Aviation Walk – 60% complete 321 Pedestrian Bridge Installed lighting, handrail, fencing remaining


Elevated Boardwalk complete Sidewalk complete from 13th Ave Dr NW to Crawdad's Stadium

City Walk Extension (Downtown Portion of Aviation Walk Project) anticipated completion fall 2023








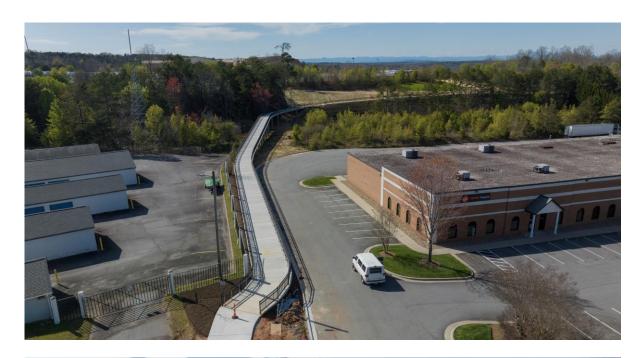



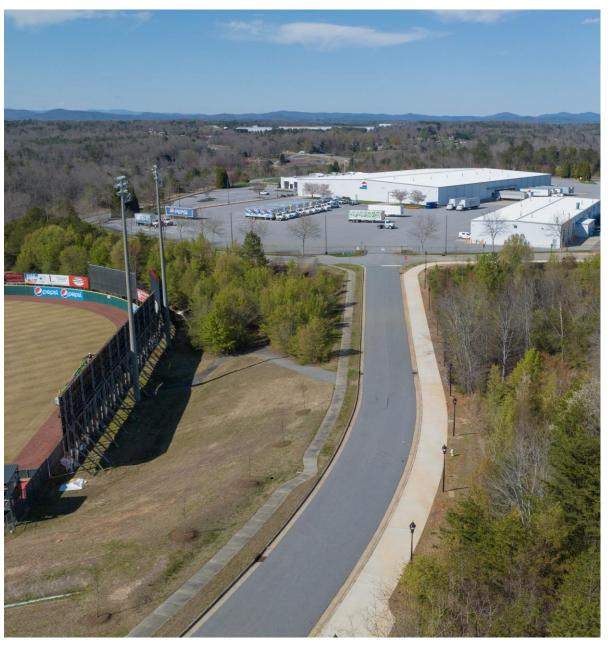













Historic Ridgeview Walk

Advertised for Construction – March 16th Open Bids – Mid-April Construction is anticipated to begin this summer.

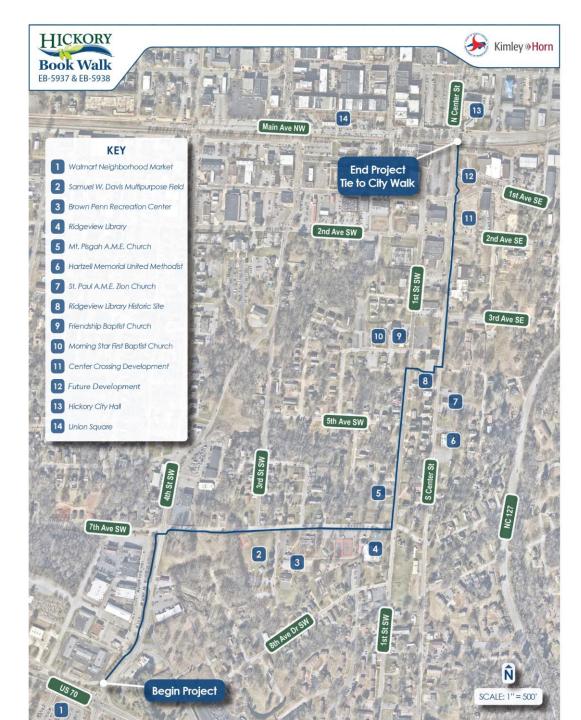

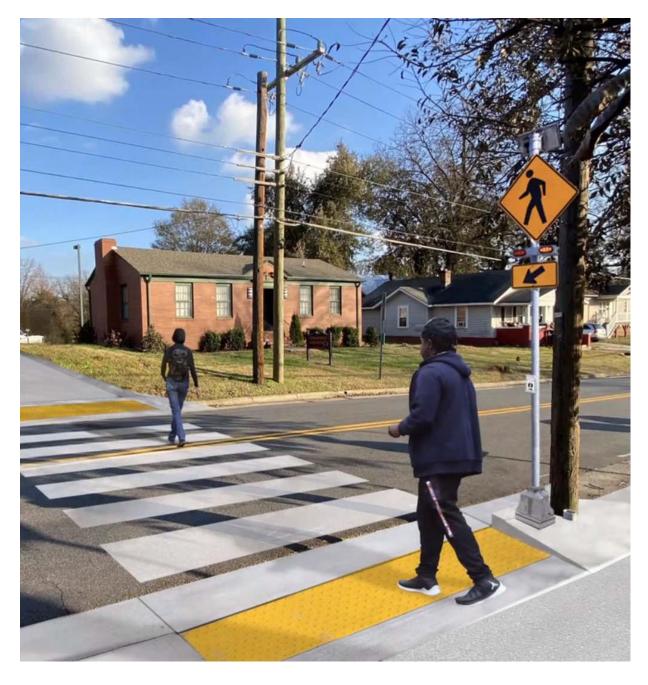






OLLE Art Walk

Advertise for Construction – Summer 2023 Open Bids – Summer 2023 Construction is anticipated to begin this fall 2023

ALIGNMENT MAP

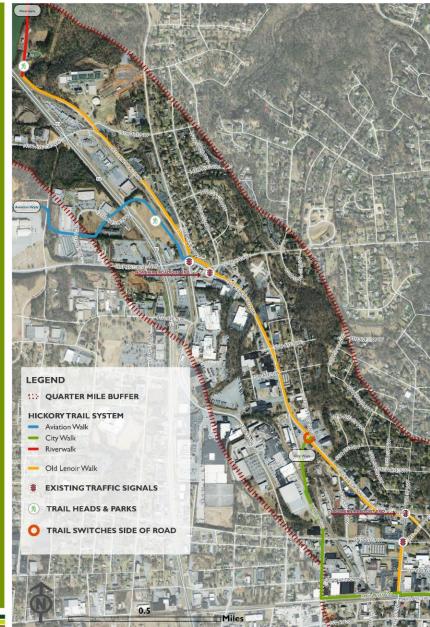











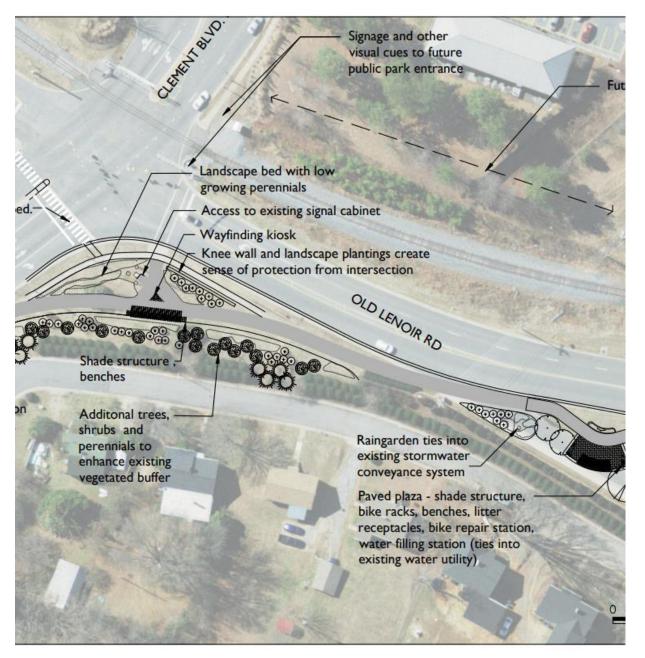

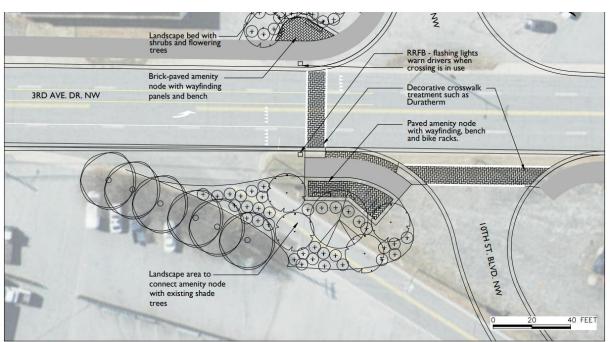



Trivium Corporate Center

The original portion of Trivium is complete except for some lighting work.

Trivium East grading is complete.

The site has bids out for sewer lines.







